

**A GUIDE TO  
STRENGTHENING PROJECT  
MANAGEMENT AND PERFORMANCE**

**APEC EDUCATION FORUM  
HUMAN RESOURCES DEVELOPMENT WORKING GROUP**


**JANUARY 1999**



**EXHIBITS**

Exhibit 2. Examples of Project Products and Measures of Results ..... 11  
 Exhibit 3. Purposes, Objectives, Activities, and Expected Results ..... 13  
 Exhibit 4. Typical Project Tasks ..... 23  
 Exhibit 5. Types of Milestones ..... 24  
 Exhibit 6. Project Schedule for Researching Technology Transfer ..... 24  
 Exhibit 7. Possible Challenges and Solutions for Implementing the  
 Assessment Process ..... 26  
 Exhibit 8. Possible Challenges and Solutions of Communicating  
 with Partners ..... 29  
 Exhibit 9. Sample Assessment Questions ..... 36

**Exhibit 1.**

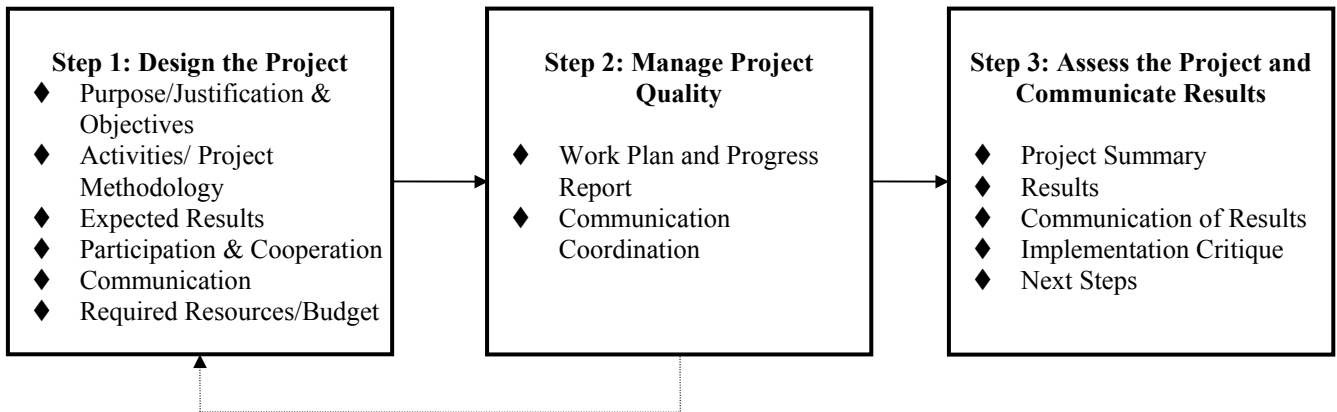

---

**THIS GUIDE WAS PREPARED FOR THE APEC HUMAN RESOURCES  
DEVELOPMENT WORKING GROUP WITH THE ADVICE OF AN  
AD HOC TASK FORCE ON PERFORMANCE MEASUREMENT, INCLUDING**

**DR. CHARLES BARRETT, CONFERENCE BOARD, CANADA  
MS. ELIZABETH EPEL, MINISTRY OF EDUCATION, NEW ZEALAND  
MR. TONY REYNALDS, MANPOWER & TRAINING, HONG KONG  
MR. KEIGOH TABIRA, FOREIGN AFFAIRS, JAPAN**

**PREPARED FOR APEC BY**

**THE U.S. DEPARTMENT OF EDUCATION  
ALAN GINSBURG**

**AND**

**THE PELAVIN RESEARCH CENTER, AT THE AMERICAN  
INSTITUTES FOR RESEARCH  
DIANE PELAVIN, NATALIA PANE, SHELLEY  
KIRKPATRICK, SYLVIA ELLISON**

**AND SPECIAL THANKS TO**

**LENORE GARCIA, AUDREY PENDLETON, AND MARIANN LEMKE; U.S. DEPARTMENT OF  
EDUCATION;**

**DAN LEMAIRE AND JOANNE WARREN, CONFERENCE BOARD OF CANADA; AND  
JAY MOSKOWITZ, ANDY ROSE, MARSHA JONES PELAVIN RESEARCH CENTER, AIR**

---

---

---

# TABLE OF CONTENTS

---

---

<b>INTRODUCTION .....</b>	<b>3</b>
<b>STEP 1. DESIGN THE PROJECT .....</b>	<b>5</b>
Purpose/ Justification and Objectives.....	6
Activities/ Project Methodology.....	7
Expected Results.....	8
Participation and Cooperation .....	14
Communication.....	14
Required Resources/ Budget.....	17
Checklist for Designing the Project.....	19
<b>STEP 2. MANAGE PROJECT QUALITY .....</b>	<b>20</b>
Work Plan and Progress Report.....	21
Coordination of Communication .....	28
Checklist for Managing Project Quality .....	32
<b>STEP 3. ASSESS THE PROJECT AND COMMUNICATE THE RESULTS.....</b>	<b>33</b>
Project Summary.....	34
Results.....	35
Communication of Results.....	37
Critique of Implementation.....	37
Next Steps.....	38
Checklist for Assessing the Project and Communicating Findings.....	39
<b>GLOSSARY .....</b>	<b>40</b>
<b>APPENDIX A. APEC PROJECT FORMS</b>	
<b>APPENDIX B. GENERAL PROJECT MANAGEMENT FORMS</b>	
<b>APPENDIX C. SAMPLE EXEMPLARY PROJECT FORMS</b>	
<b>APPENDIX D. GUIDE TO GENDER-BASED ANALYSIS</b>	
<b>APPENDIX E. HRDWG's STRATEGIC AND MEDIUM     TERM PRIORITIES AND APEC 1996 MANILA DECLARATION</b>	
<b>APPENDIX E. SUGGESTIONS FOR FURTHER READING</b>	
